


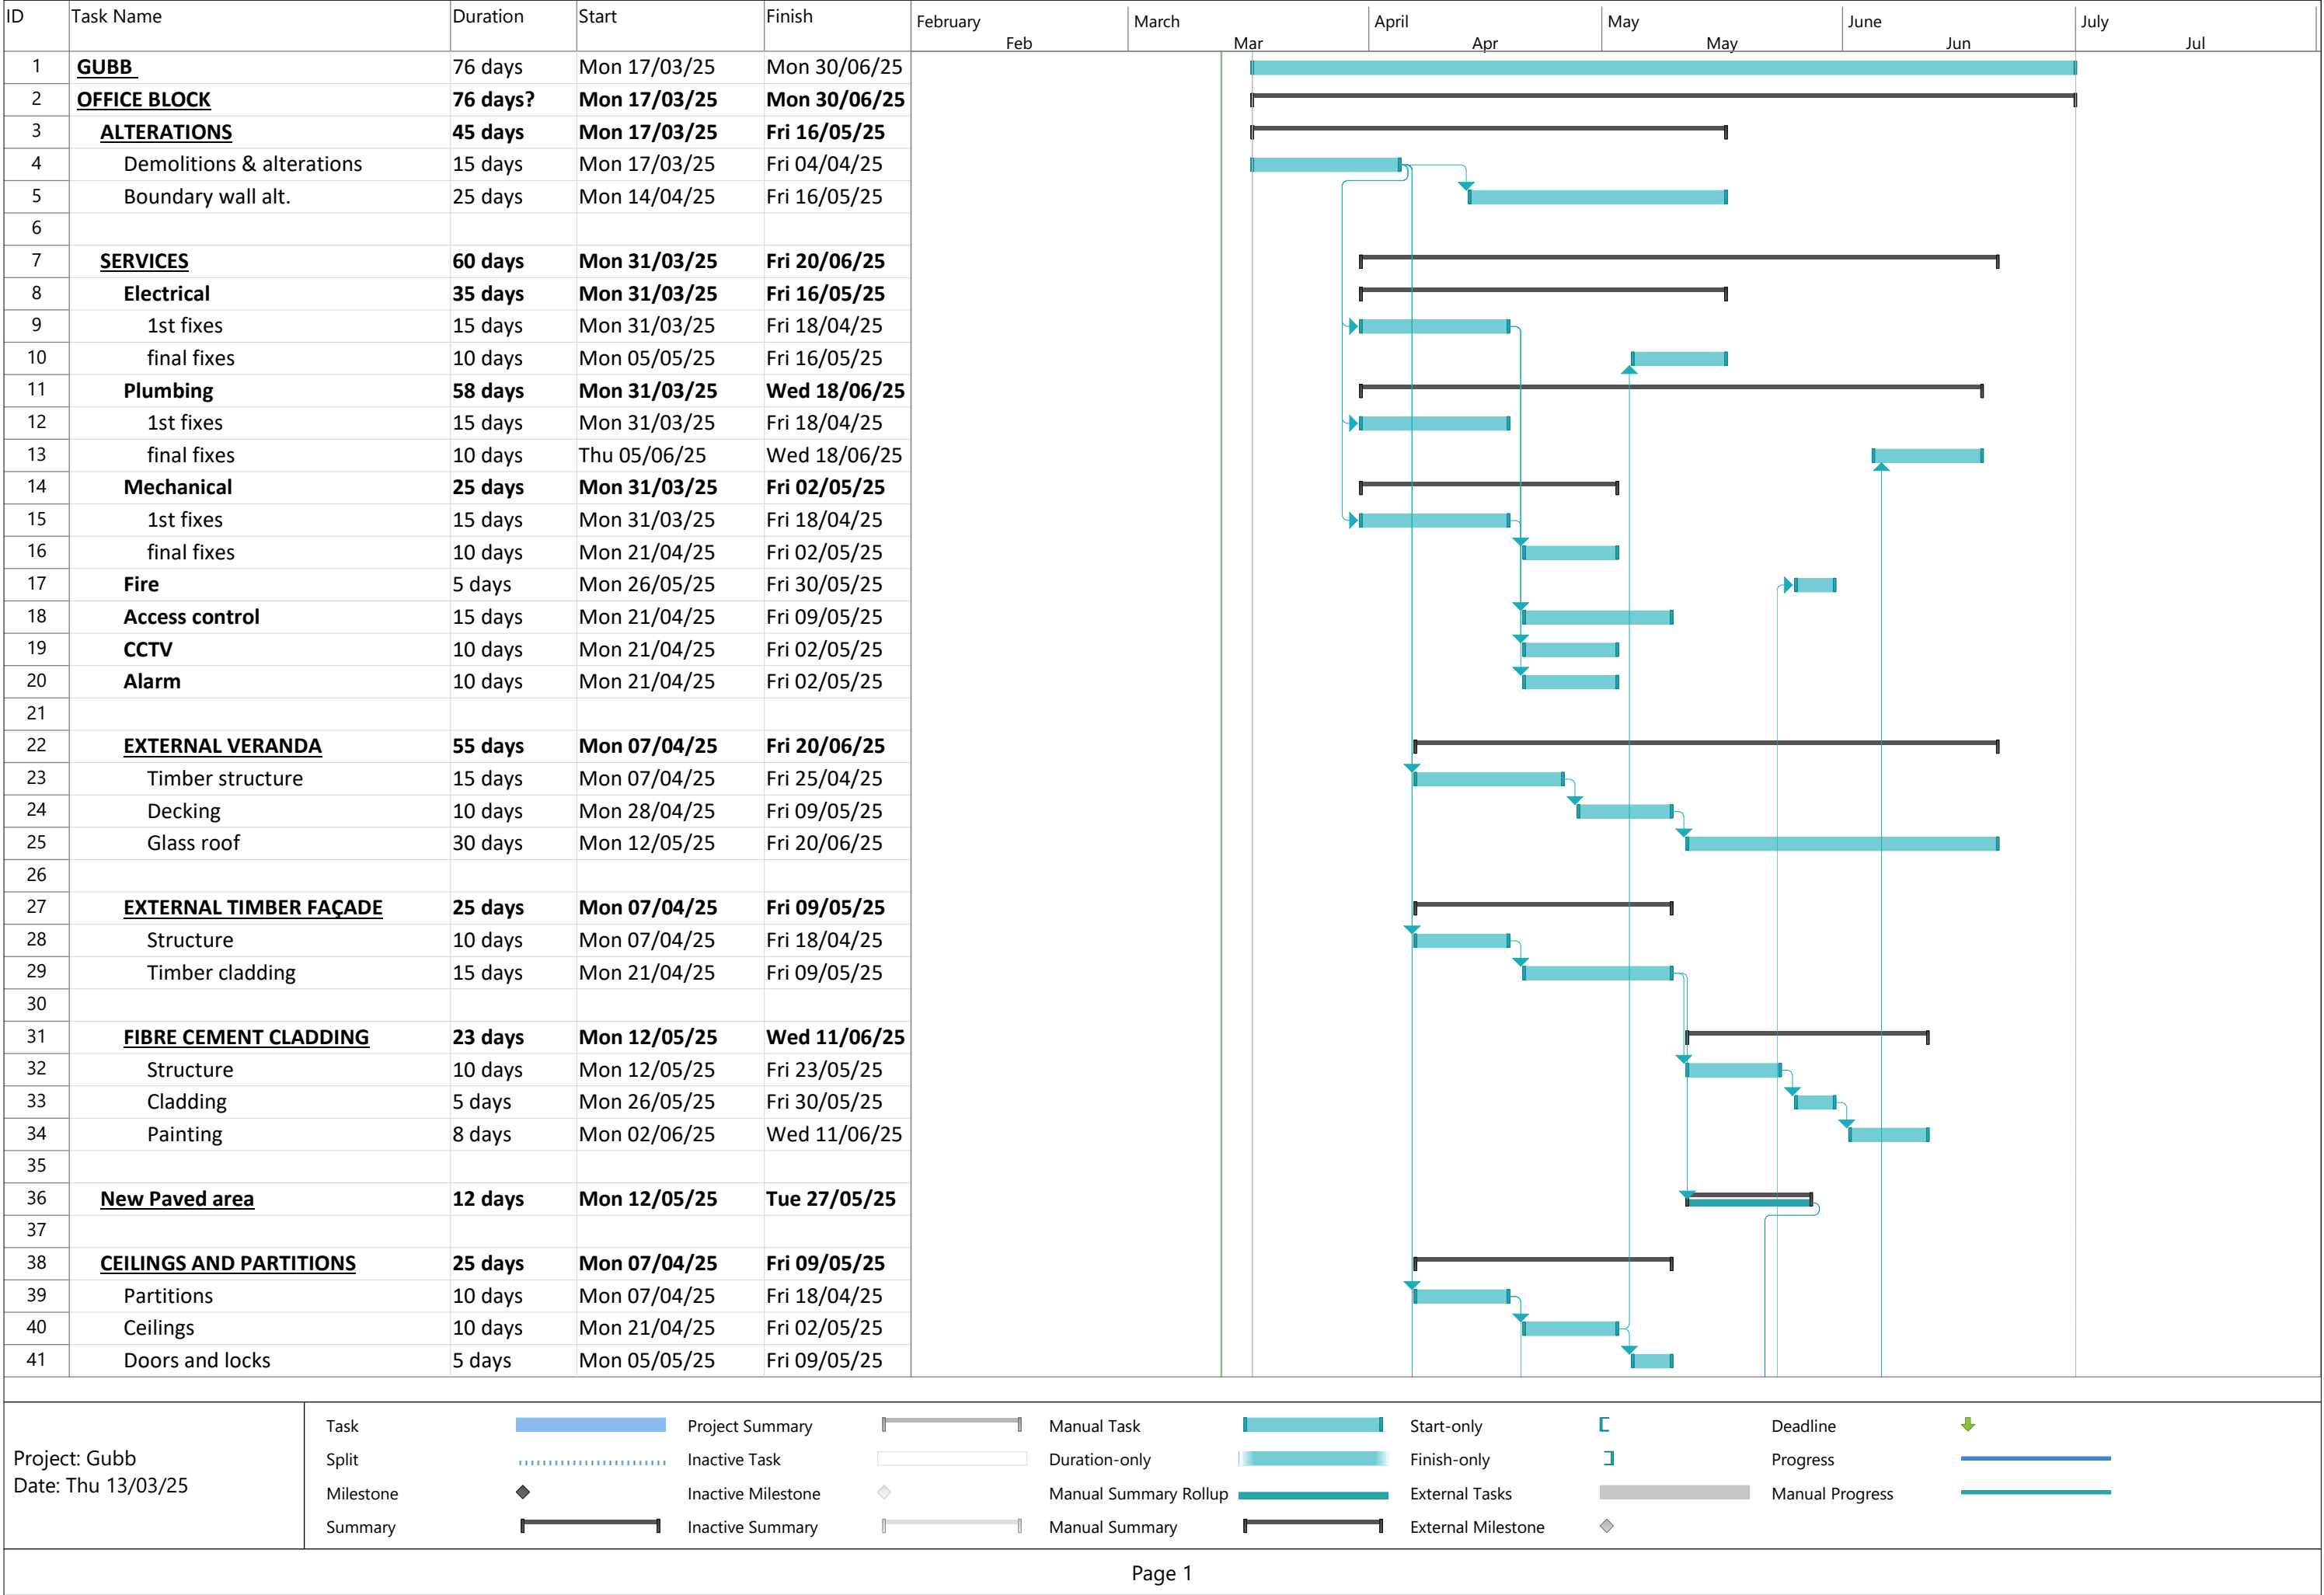

ID	Task Name	Duration	Start	Finish	February Feb	March Mar	April Apr	May May	June Jun	July Jul
42										
43	PAINTING	45 days	Mon 21/04/25	Fri 20/06/25						
44	1st coats	15 days	Mon 21/04/25	Fri 09/05/25						
45	finals coats	15 days	Mon 12/05/25	Fri 30/05/25						
46	External	15 days	Mon 02/06/25	Fri 20/06/25						
47	Wall paper	5 days	Mon 02/06/25	Fri 06/06/25						
48										
49	TILING	20 days	Mon 07/04/25	Fri 02/05/25						
50	Floor tiling	10 days	Mon 07/04/25	Fri 18/04/25						
51	Wall tiling	10 days	Mon 21/04/25	Fri 02/05/25						
52										
53	JOINERY	43 days	Mon 07/04/25	Wed 04/06/25						
54	Manufacture	30 days	Mon 07/04/25	Fri 16/05/25						
55	Install	18 days	Mon 12/05/25	Wed 04/06/25						
56										
57	CARPETS	55 days	Mon 07/04/25	Fri 20/06/25						
58	Procure	20 days	Mon 07/04/25	Fri 02/05/25						
59	Install	5 days	Mon 16/06/25	Fri 20/06/25						
60										
61	SUNDRIES	54 days	Mon 07/04/25	Thu 19/06/25						
62	Blinds	45 days	Mon 07/04/25	Fri 06/06/25						
63	Order	10 days	Mon 07/04/25	Fri 18/04/25						
64	Install	5 days	Mon 02/06/25	Fri 06/06/25						
65	Mirrors	12 days	Mon 12/05/25	Tue 27/05/25						
66	Order	5 days	Mon 12/05/25	Fri 16/05/25						
67	Install	2 days	Mon 26/05/25	Tue 27/05/25						
68	Bathroom fittings	21 days	Mon 12/05/25	Mon 09/06/25						
69	Order	15 days	Mon 12/05/25	Fri 30/05/25						
70	Install	3 days	Thu 05/06/25	Mon 09/06/25						
71										
72	Signage	25 days	Mon 12/05/25	Fri 13/06/25						
73	Procure	15 days	Mon 12/05/25	Fri 30/05/25						
74	Install	5 days	Mon 09/06/25	Fri 13/06/25						
75										
76	Flagpole	54 days	Mon 07/04/25	Thu 19/06/25						
77	Base	12 days	Mon 07/04/25	Tue 22/04/25						
78	Procure	40 days	Wed 23/04/25	Tue 17/06/25						
79	Installation	2 days	Wed 18/06/25	Thu 19/06/25						
80										
81	Landscaping	12 days	Fri 23/05/25	Tue 10/06/25						
82										

Project: Gubb

Date: Thu 13/03/25

Task

Split

Milestone

Summary

◆

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

◆

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

[

]

◆


Deadline

Progress

Manual Progress

↓

Page 2

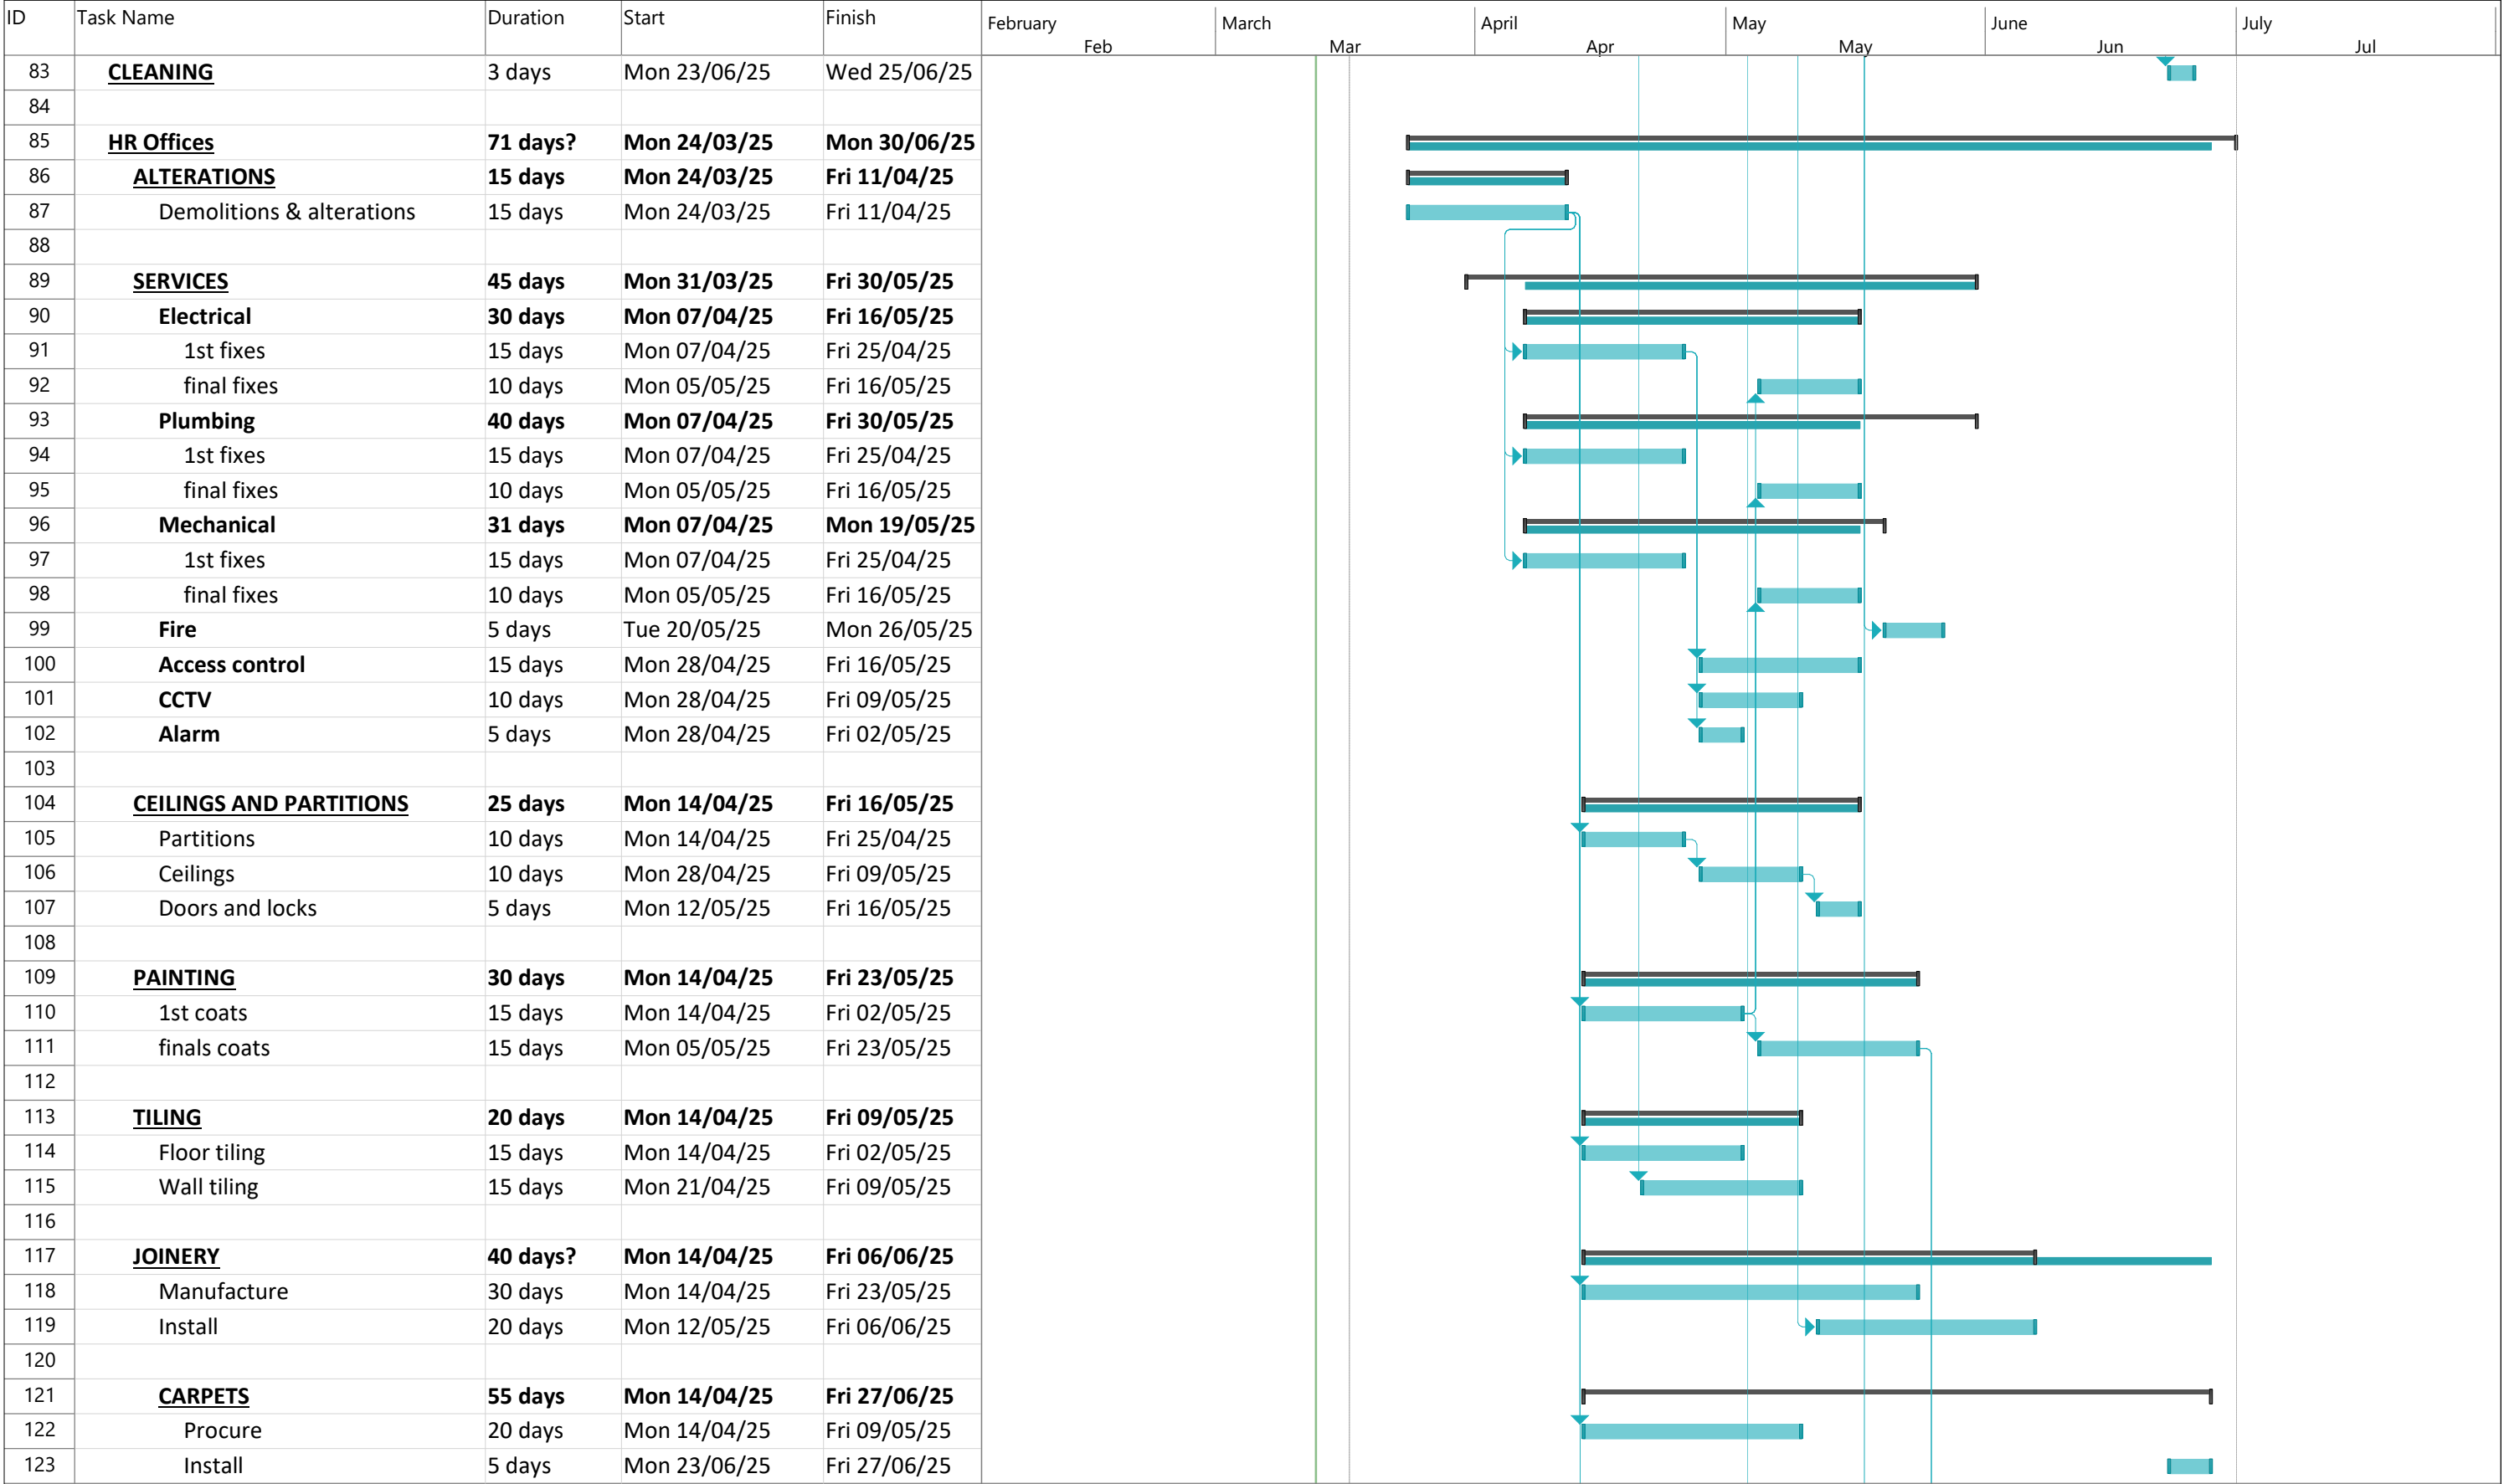

Project: Gubb
Date: Thu 13/03/25

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only


External Tasks

External Milestone

Deadline

Progress

Manual Progress

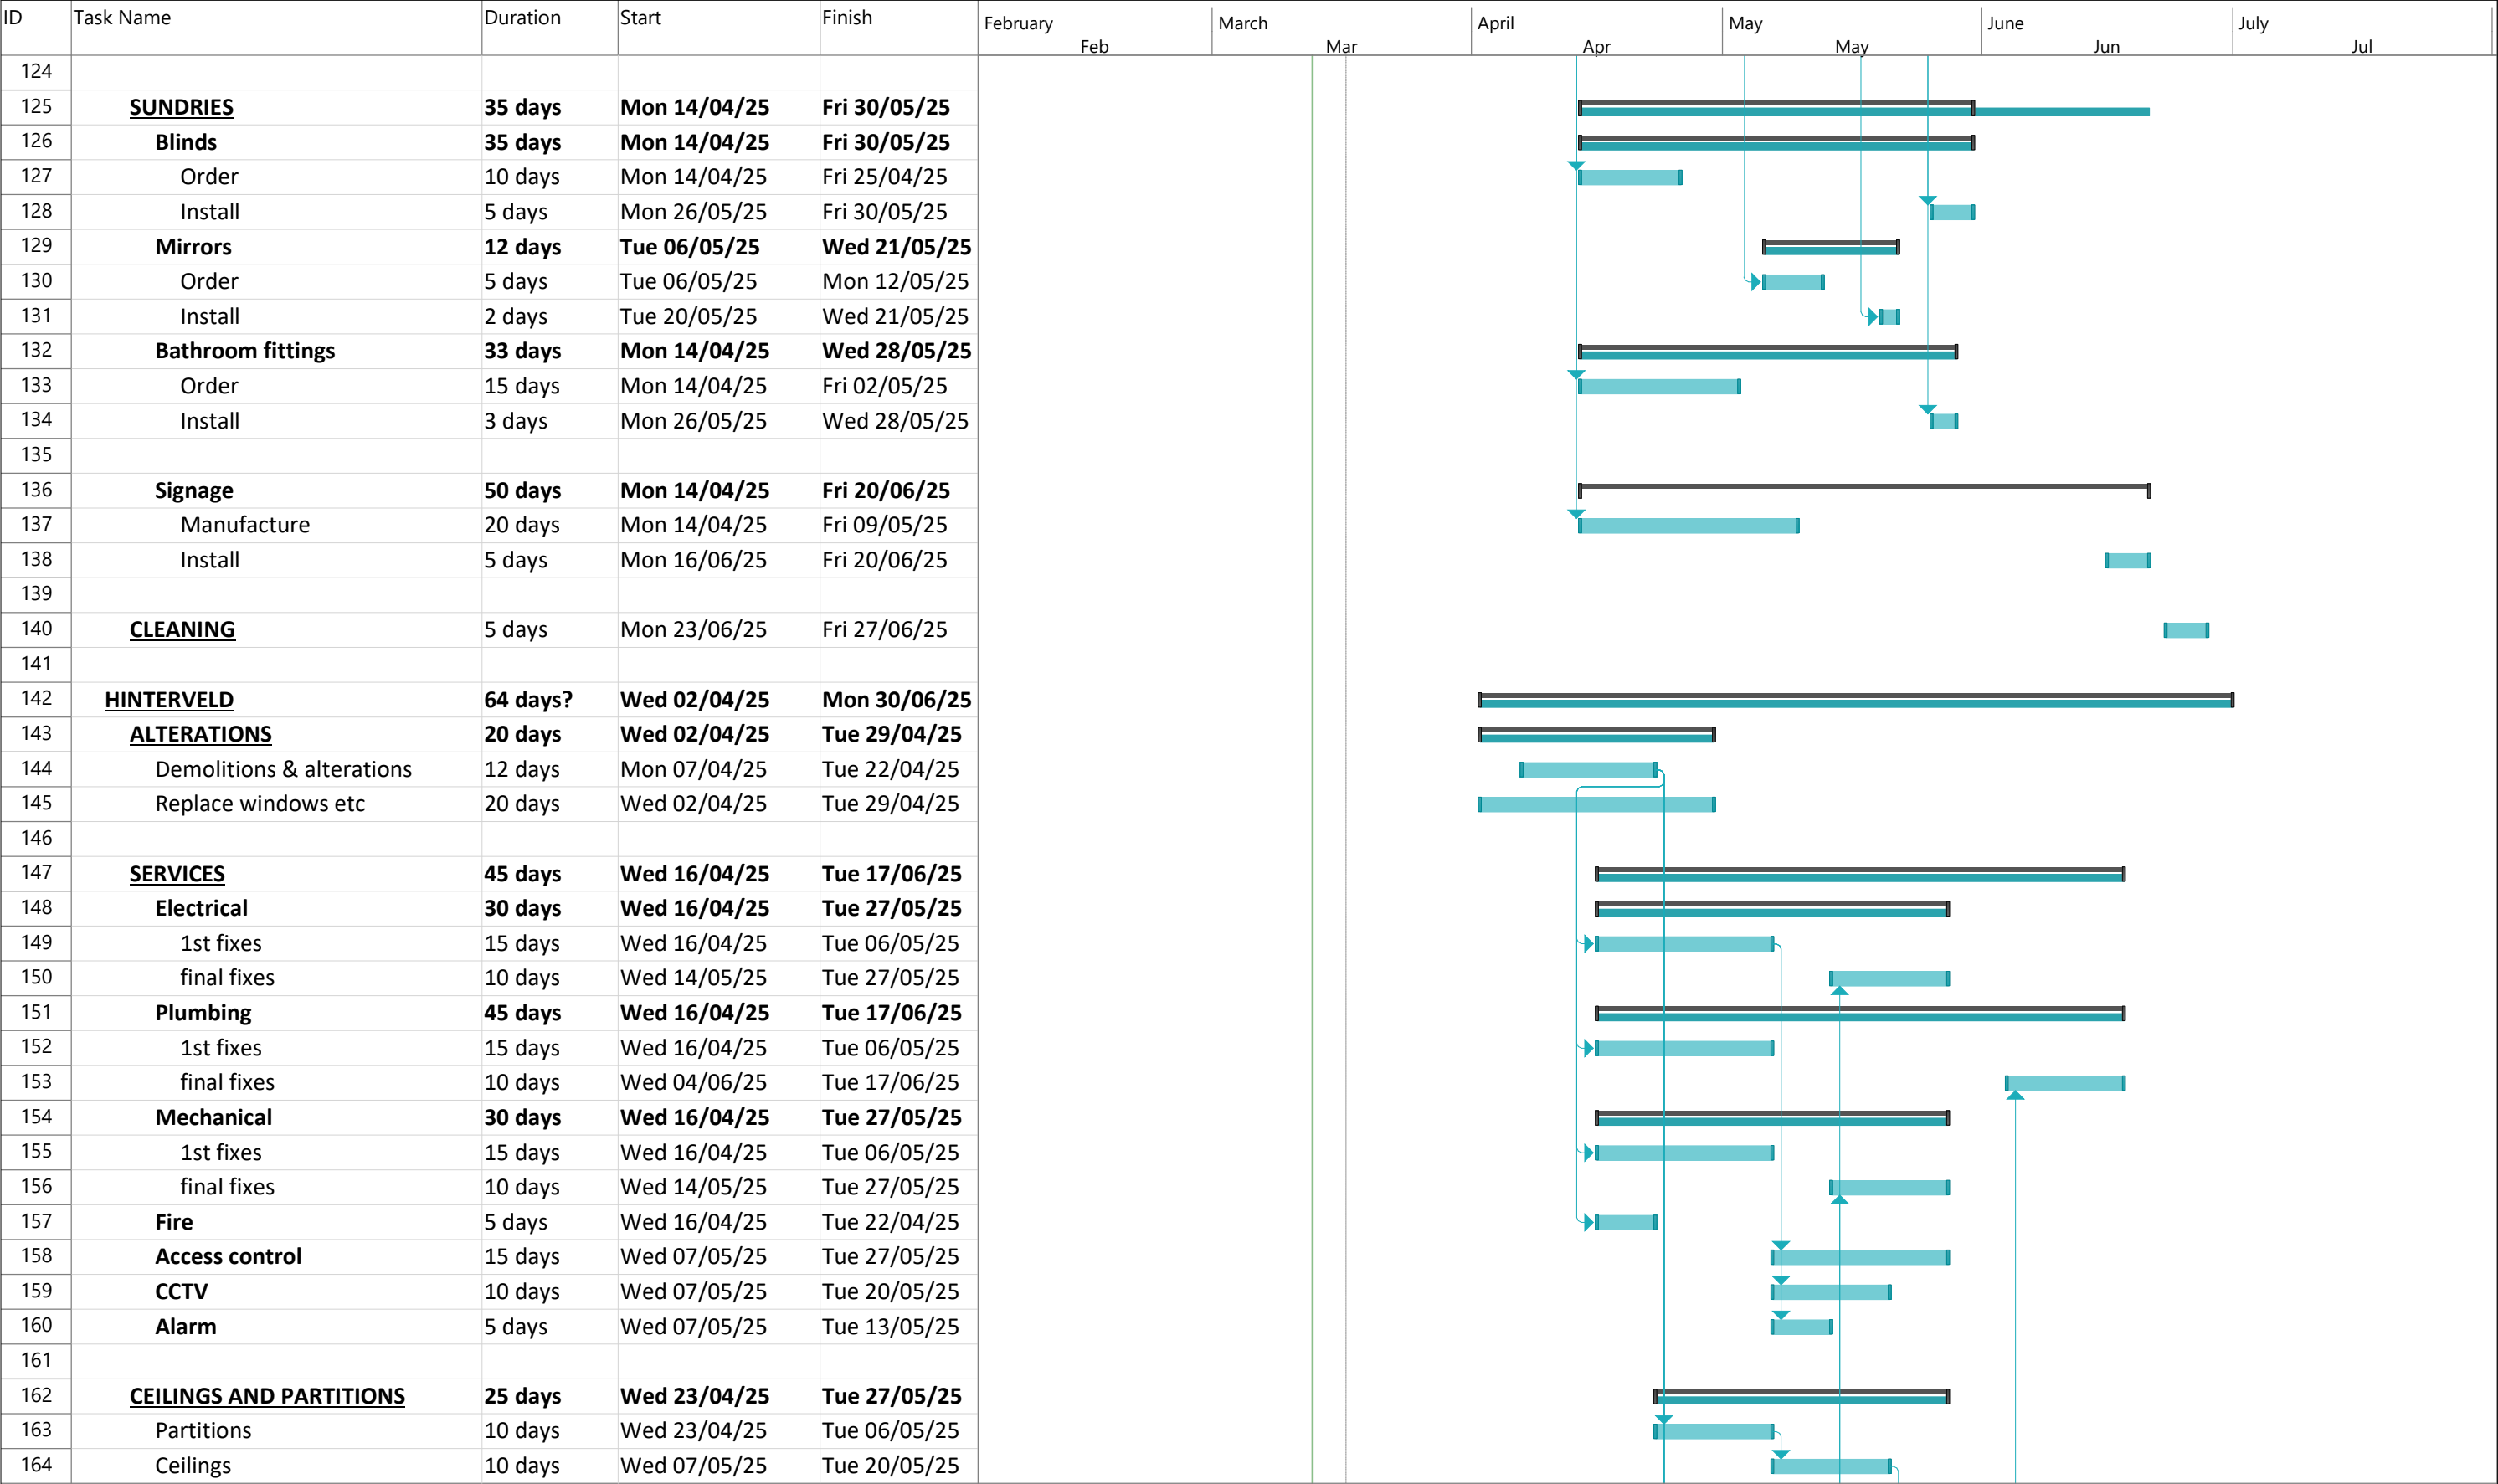

ID	Task Name	Duration	Start	Finish	February Feb	March Mar	April Apr	May May	June Jun	July Jul
165	Doors and locks	5 days	Wed 21/05/25	Tue 27/05/25						
166										
167	PAINTING	45 days	Wed 23/04/25	Tue 24/06/25						
168	1st coats	15 days	Wed 23/04/25	Tue 13/05/25						
169	finals coats	15 days	Wed 14/05/25	Tue 03/06/25						
170	External	15 days	Wed 04/06/25	Tue 24/06/25						
171										
172	TILING	30 days	Wed 23/04/25	Tue 03/06/25						
173	Floor tiling	15 days	Wed 23/04/25	Tue 13/05/25						
174	Wall tiling	15 days	Wed 14/05/25	Tue 03/06/25						
175										
176	JOINERY	48 days	Wed 23/04/25	Fri 27/06/25						
177	Manufacture	30 days	Wed 23/04/25	Tue 03/06/25						
178	Install	18 days	Wed 04/06/25	Fri 27/06/25						
179										
180	DECKING AND BENCH	25 days	Wed 23/04/25	Tue 27/05/25						
181	Procure	15 days	Wed 23/04/25	Tue 13/05/25						
182	Install	10 days	Wed 14/05/25	Tue 27/05/25						
183										
184	TIMBER FLOORING	35 days	Wed 23/04/25	Tue 10/06/25						
185	Procure	20 days	Wed 23/04/25	Tue 20/05/25						
186	Install	10 days	Wed 28/05/25	Tue 10/06/25						
187										
188	CARPETS	43 days	Wed 23/04/25	Fri 20/06/25						
189	Procure	20 days	Wed 23/04/25	Tue 20/05/25						
190	Install	5 days	Mon 16/06/25	Fri 20/06/25						
191										
192	SUNDRIES	37 days?	Wed 23/04/25	Thu 12/06/25						
193	Blinds	15 days	Wed 23/04/25	Tue 13/05/25						
194	Order	10 days	Wed 23/04/25	Tue 06/05/25						
195	Install	5 days	Wed 07/05/25	Tue 13/05/25						
196	Mirrors	39 days	Mon 21/04/25	Thu 12/06/25						
197	Order	5 days	Wed 04/06/25	Tue 10/06/25						
198	Install	2 days	Wed 11/06/25	Thu 12/06/25						
199	Bathroom fittings	33 days	Wed 23/04/25	Fri 06/06/25						
200	Order	15 days	Wed 23/04/25	Tue 13/05/25						
201	Install	3 days	Wed 04/06/25	Fri 06/06/25						
202										
203	SIGNAGE	25 days	Wed 14/05/25	Tue 17/06/25						
204	Manufacture	20 days	Wed 14/05/25	Tue 10/06/25						
205	Install	5 days	Wed 11/06/25	Tue 17/06/25						

Project: Gubb
Date: Thu 13/03/25

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

Page 5

ID	Task Name	Duration	Start	Finish	February Feb	March Mar	April Apr	May May	June Jun	July Jul
206										
207	<u>Landscapping</u>	12 days	Mon 02/06/25	Tue 17/06/25						
208										
209	<u>CLEANING</u>	4 days	Wed 25/06/25	Mon 30/06/25						

Project: Gubb Date: Thu 13/03/25	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			
